


X:\FL\State Folder Base Plans\FL_BCAD\Projects_01-31-2012.dwg, PDF, vswantz

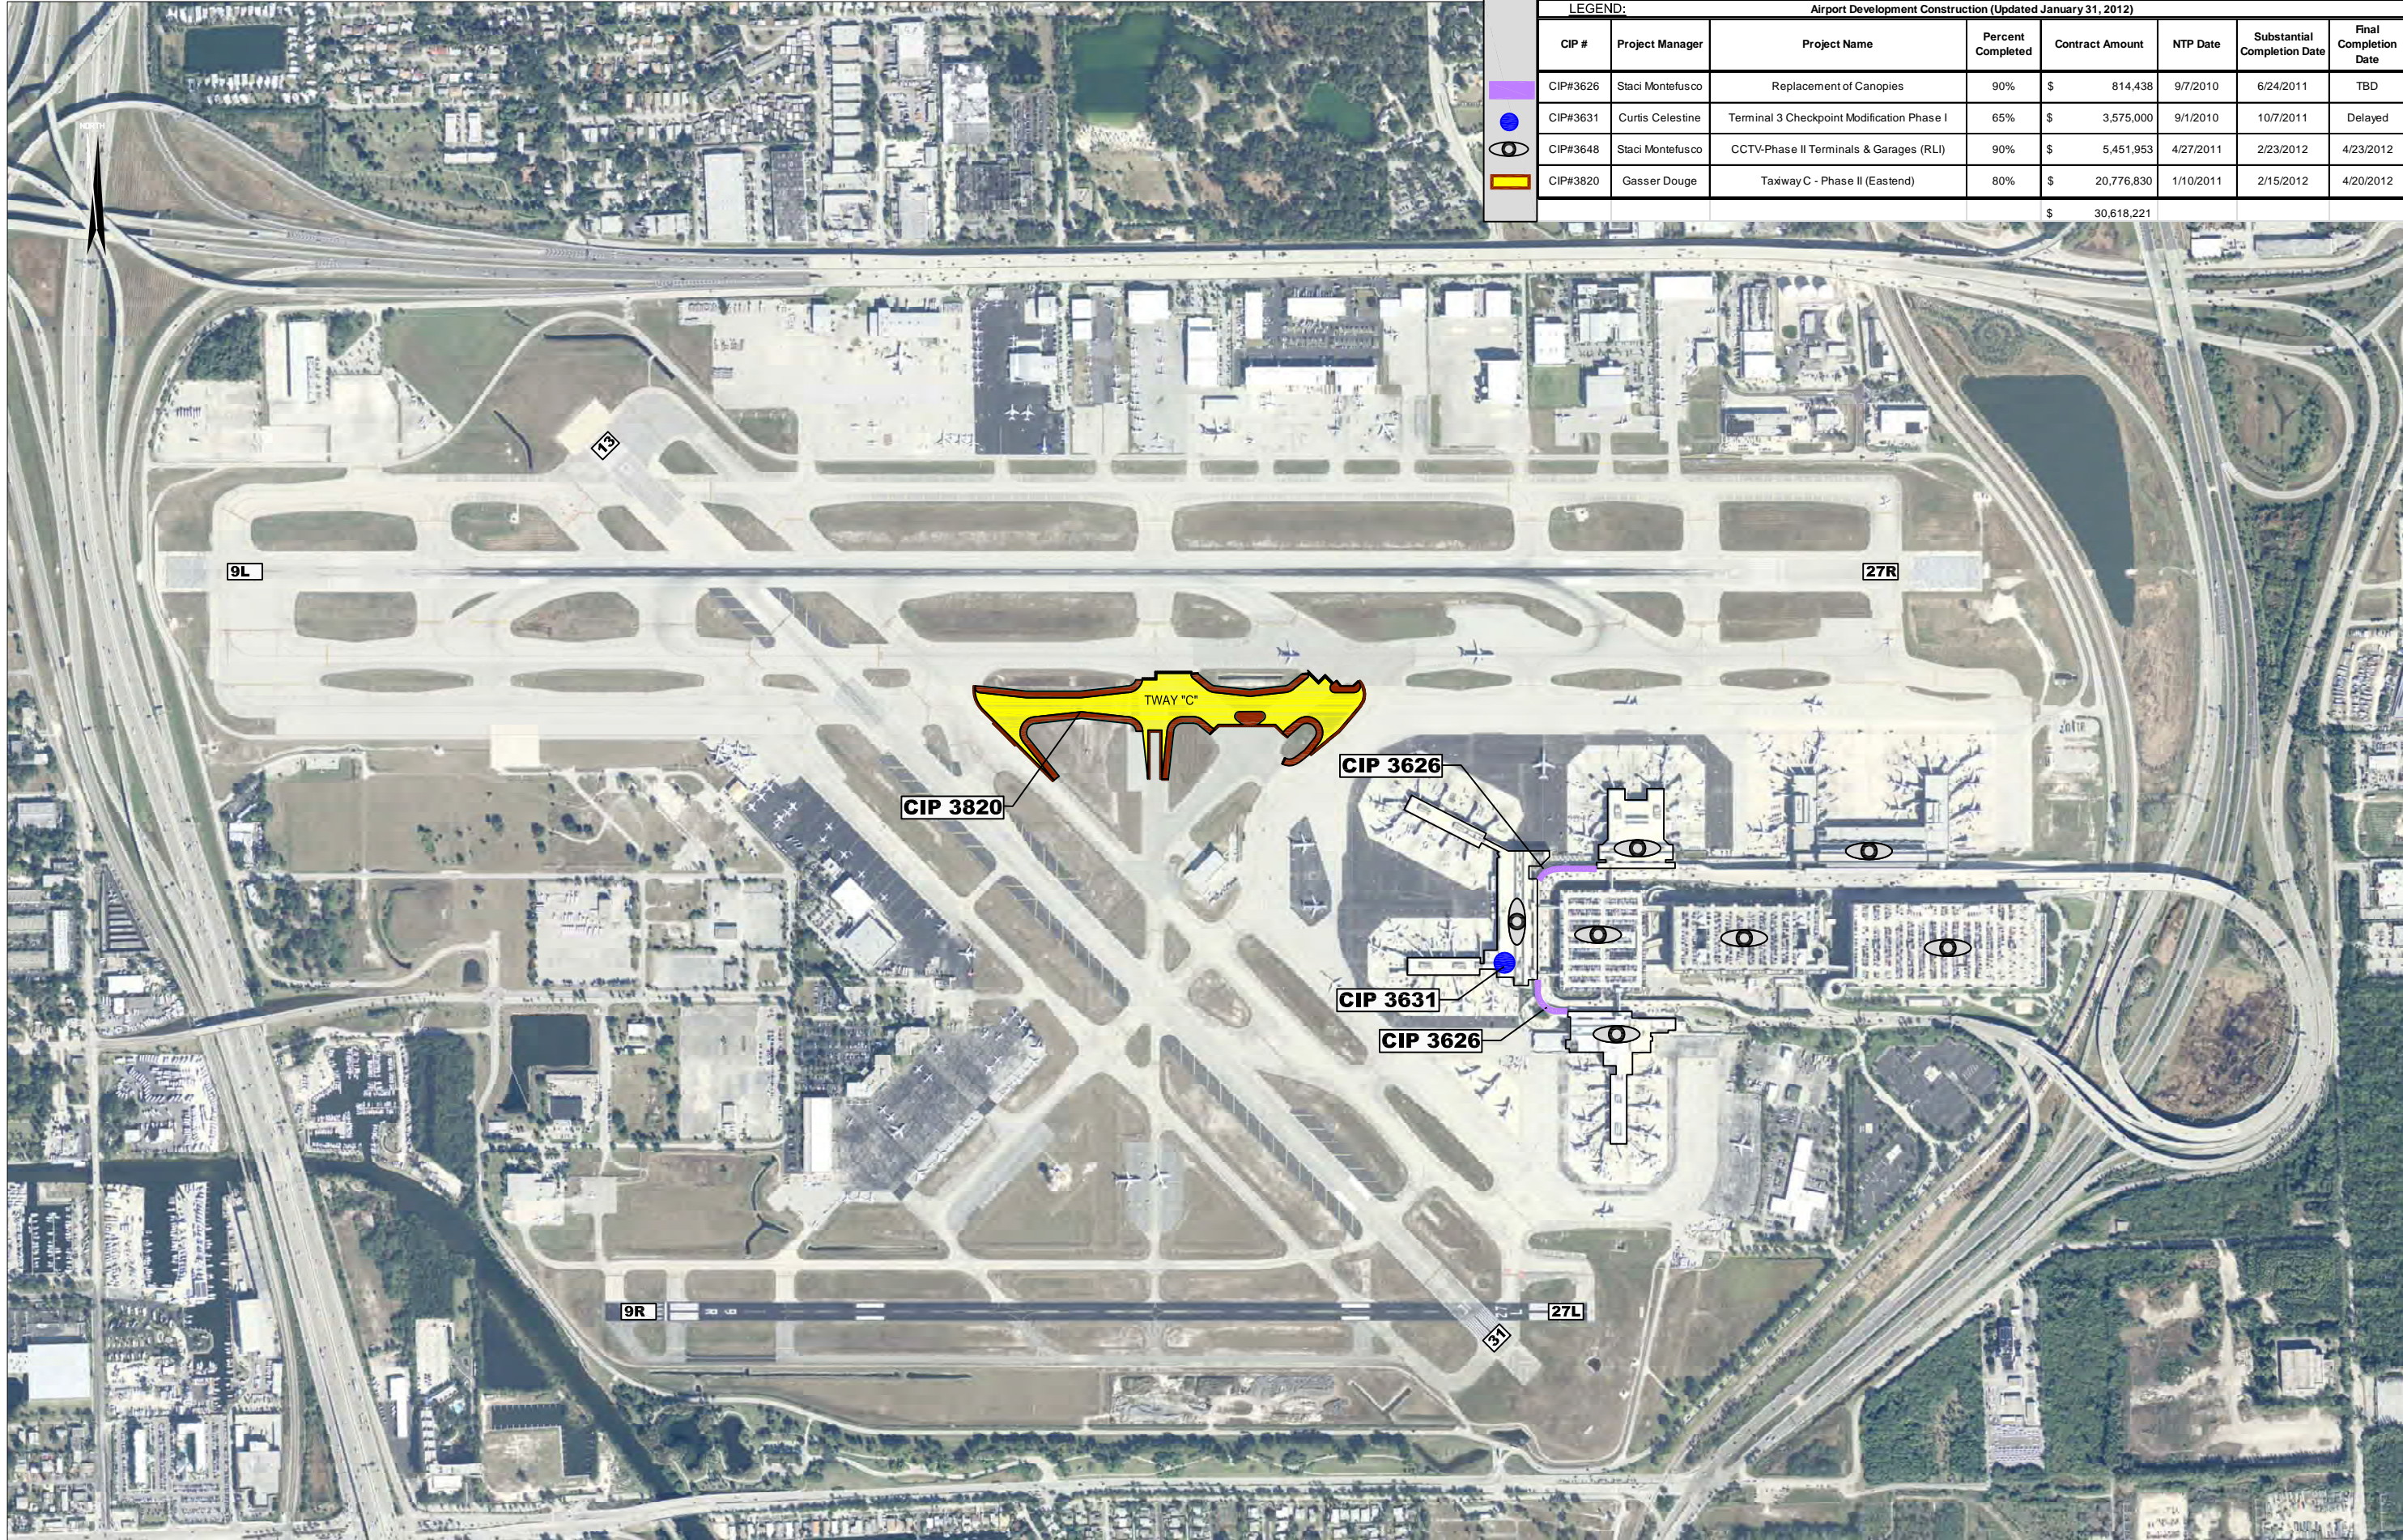

LEGEND: Airport Development Construction (Updated January 31, 2012)							
CIP #	Project Manager	Project Name	Percent Completed	Contract Amount	NTP Date	Substantial Completion Date	Final Completion Date
CIP#3626	Staci Montefusco	Replacement of Canopies	90%	\$ 814,438	9/7/2010	6/24/2011	TBD
CIP#3631	Curtis Celestine	Terminal 3 Checkpoint Modification Phase I	65%	\$ 3,575,000	9/1/2010	10/7/2011	Delayed
CIP#3648	Staci Montefusco	CCTV-Phase II Terminals & Garages (RLI)	90%	\$ 5,451,953	4/27/2011	2/23/2012	4/23/2012
CIP#3820	Gasser Douge	Taxiway C - Phase II (Eastend)	80%	\$ 20,776,830	1/10/2011	2/15/2012	4/20/2012
				\$ 30,618,221			

DATE	BY	REVISION
07/07/12	CP	
07/09/12	CP	
08/10/12	CP	
07/10/12	CP	

FORT LAUDERDALE-HOLLYWOOD INTERNATIONAL AIRPORT (FL)
 Airport Development Construction Projects



BROWARD COUNTY
 PLANNING & DEVELOPMENT DIV.
 100 MANNA RD., LAUDERHILL, FL 33309

DATE	07/15/10
DESIGNER	MSJUREZ
SCALE	AS SHOWN
FILE NO.	0000-00
PROJECT NO.	0000-00

Airport Development Construction (Updated January 31, 2012)

CIP #	Project Manager	Project Name	Percent Completed	Contract Amount	NTP Date	Substantial Completion Date	Final Completion Date
CIP#3626	Staci Montefusco	Replacement of Canopies	90%	\$ 814,438	9/7/2010	6/24/2011	TBD
CIP#3631	Curtis Celestine	Terminal 3 Checkpoint Modification Phase I	65%	\$ 3,575,000	9/1/2010	10/7/2011	Delayed
CIP#3648	Staci Montefusco	CCTV-Phase II Terminals & Garages (RLI)	90%	\$ 5,451,953	4/27/2011	2/23/2012	4/23/2012
CIP#3820	Gasser Douge	Taxiway C - Phase II (Eastend)	80%	\$ 20,776,830	1/10/2011	2/15/2012	4/20/2012

\$ 30,618,221
